





Roahe Rainbow Bridge <https://pixabay.com/photos/raohe-rainbow-bridge-the-dark-night-2843988/>

Moving of the Third Office


Lien Yang



Written by Prosecutor Investigator, Lien Yang, who also supervised construction of the Project.




- I Background
- II Reasons and Source of Funds
- III Basic Information of the Project
- IV Pre-Renovation Status Survey
- V Pre-Renovation Floor Plan and Photos
- VI Post-Renovation Floor Plan and Photos
- VII Important Milestones
- VIII Process of Design Changes
- IX Project Difficulties and Solutions
- X Project Supervision Team and Supervision Records
- XI Set-Up Process of Office 3 and Digital Evidence Collection Room
- XII Opening Ceremony of Office 3 and Digital Evidence Collection Room



I. Background

Office 3 was originally located at 1&2/F, No. 185, Section 2, Xinhai Road, Da'an District, Taipei City (Central Baishi Building), which is considerable far from the Office. In view of the fact that the office building of the Office is not enough for use and the new judicial building where the Office is located is restricted for expansion, therefore, the only option was to request the appropriation of nearby available public building from National Property Administration, Ministry of Finance to renovate and use, in order to save huge amount of rent required for renting office buildings and be able to effectively manage the office. The public building appropriated for the Office 3 renovation project is located at the Procurement Building of the Ministry of National Defense (No. 172-1, Bo'ai Road, Zhongzheng District, Taipei City). The land is a state-owned property and the manager was Armaments Bureau, Ministry of National Defense. Upon the persistent effort of Ministry of Justice, Executive Yuan agreed to appropriate the building to the Office after Ministry

of National Defense moved to Dazhi Boai Camp. After the building completed the approved relevant renovation and procurement pursuant to the provisions of the Government Procurement Act and Prosecutor Investigators of the primary user units moved in, people who contact the Office for business or court session can avoid the inconvenience caused by going to the wrong office. After the Office added more Investigation Rooms in the space vacated, it further solved the Investigation Room shortage issue and the difficulty of having to queue up to use the Investigation Room which delays the investigation, while improving the investigation efficiency in respond to the increasing amount of procuratorial business, as well as improving the judicial quality, promoting social justice, greatly benefiting the quality and performance of case-solving, the promotion of rule of law, litigation counseling and other aspects of works, and making it convenient for the people to contact for business.




II. Reasons and Source of Funds

1. In accordance with the approval and instruction specified in Document No.Fa-Zong-10401505530 issued by the Ministry of Justice on 25 June 2015 concerning the "Renovation Project Plan and Estimated Budget for the Construction of Additional Investigation Room to the Office Building and Old Offices in the Procurement Building of Taiwan Taipei District Court Prosecutors Office".
2. Total costs of the plan approved by the Executive Yuan:

The cost of the plan was original budgeted at the amount of NT\$79,737,141 on 25 June 2015. However, upon the negotiation during the meeting with the Ministry of National Defense on 16 February 2016, the Ministry of National Defense required the installation of

louver protection and shielding facilities on the side facing the military camp and keeping its mailroom at 1/F of Building B. In addition, since the original design plan did not take water seepage of the doors & windows, typhoon damages on 4/F rebar truss roof and carcinogenic issue of asbestos building materials into account, therefore the original design plan shall be adjusted to add the door/window project, the louver protection and shielding project, replace the asbestos tile and other projects. After the Office submitted the revised plan to Taiwan High Prosecutors Office on 25 March 2016 for review by the Ministry of Justice and Executive Yuan, the Executive Yuan issued Document No.Yuan-Shou-Zhu-Yu-Zheng-1050101147 on 23 May 2016 approving the revised total costs of NT\$92,702,000 for the plan.

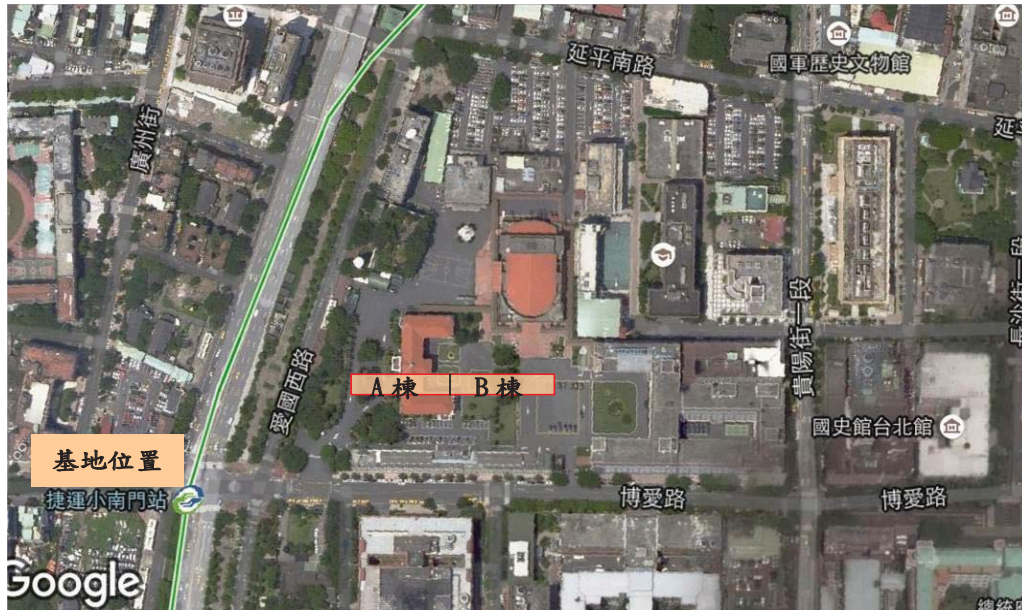

III. Basic Information of the Project

A. Construction year: 1964

B. Building type: RC buildings (Building A & B)

C. Storey: 4 floors above ground, 1 floor underground

D. Total floor area (m2): 4739.72 m2

Total floor area of the 4 floors above ground (m2): 4266.53 m2

Total floor area of the basement floor (m2): 473.19m2

E. Seismic assessment:

1. Building A

Detailed assess of the original building:

X-direction A_p value: 0.179 g

Y-direction A_p value: 0.197 g

Post-reinforcement building:

X-direction A_p value: 0.285 g

Y-direction A_p value: 0.361 g

2. Building B

Detailed assess of the original building:


X-direction A_p value: 0.198 g

Y-direction A_p value: 0.197 g

Post-reinforcement building:

X-direction A_p value: 0.291 g

Y-direction A_p value: 0.285 g



F. Seismic reinforcement method: add 12 wing walls and 6 shear walls

G. Construction period: to be commenced on 27 November 2016 and completed on 25 November 2017


H. Commissioned design supervision unit: CHIEH CHIEN-HUA Architecture Firm

I. Name of the successful contractor: Taiyi Construction Co., Ltd.


IV. Pre-Renovation Status Survey

The Procurement Building (the Office's Office 3) is located in Bo'ai Special Zone with one basement level and four storeys. The foundation is adjacent to the Bo'ai Road connected with Building A & B, where were all completed on 24 January 1964. The four-storey building was built after 1978 and was formerly subject to the Ministry of National Defense. After the Ministry of National Defense moved to Dazhi Boai Camp in December 2014, the Procurement Building office located at No. 172-1, Bo'ai Road, Taipei City was granted upon resolution between the Executive Yuan, Ministry of National Defense and Ministry of Justice to be used by the Office.

The building was an old military building of more than 40 years old. Not only was it lack of relevant seismic resistance structural safety information, the Ministry of National Defense was also unable to provide floor plans for each floor of the building. In addition, due to issues such as the change in demand, the building was old and flooded, the main equipment were also old, the air-conditioners were relocated, overall poor equipment efficiency, and the building materials or space planning back then do not meet the requirements of the current Building Control Act and Fire Services Act, the Procurement Building required renovation or additional construction to re-plan air-conditioner with five major pipelines, fire-prevention refuge facilities, fire-fighting equipment and other construction items. The following table shows each floor prior to the renovation:

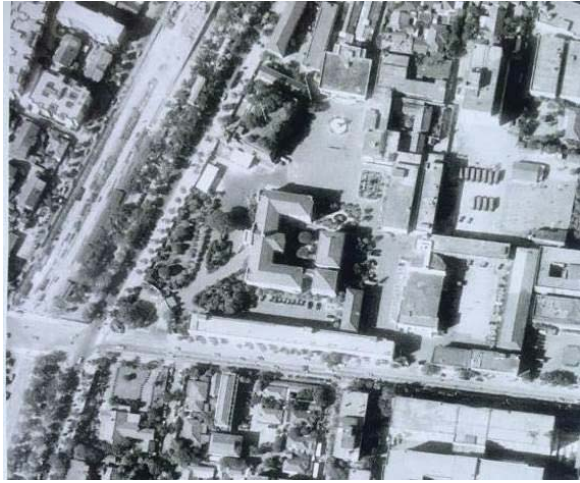


1978 aerial photograph

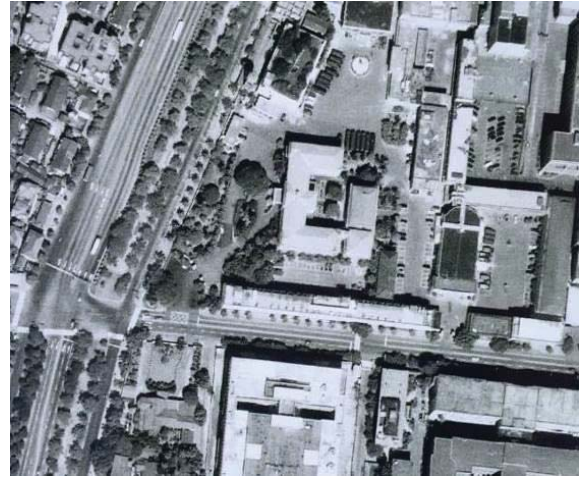


1984 aerial photograph

Floor	Overview	Remarks
B1F	Divided into Building A zone and Building B zone, each equipped with single staircase to 1/F. Building A was original used as an office space, while Building B was used for offices. Upon survey, the structural part of Building B (next to the lobby) was found backfilled with cobblestone layer.	The basement grade beam was upstand beam with severe water seepage; the floor was flooded with water up to a height of 10cm. Building B consists of an area >240 m ² and a staircase shall be added.
1F	The main entrance, that is, the left and right sides and lobby of Building A/B shall all be equipped with 1/F~2/F, 1/F~3/F and 1/F~4/F direct elevators. The original renovation plan of adding an L-shaped ladder between 1/F and 2/F requires the removal of structural beam. 1/F is equipped with air-conditioner engine room, which can be accessed for maintenance through roll-up door. The non-hallway space shall be use for work.	The main entrance of the Procurement Building is adjacent to Bo'ai Road. The building is connected to the Ministry of National Defense at the back side with one entrance each at the left and right side.
2F	Building with linear shaped office layout and unilateral hallway.	The brick wall separating the hallway and the office space was not fully constructed to the ceiling;the renovation shall strengthen it to the ceiling to form an effective fireproof compartment. The emergency staircases of the direct elevators all failed to meet the structural requirements of the emergency staircase.
3F	Building with linear shaped office layout and unilateral hallway.	
4F	This is a rebar truss structure built after 1978 using wooden partition wall to divide it into leisure spaces.	The rebar struss cover plate was asbestos tile which is carcinogens. It is adviseable to replace.



V.Pre-Renovation Floor Plan and Photos


Pre-renovation B1/F floor plan



20 November 2015: office at B1/F of Building A



20 November 2015: office at B1/F of Building A

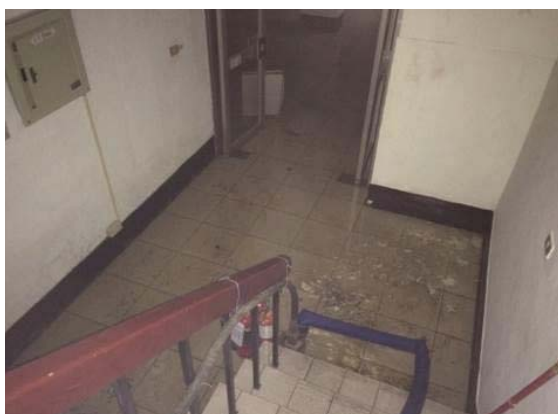

20 November 2015: flooded staircase at B1/F of Building A



20 November 2015: escape ladder at B1/F of Building A



20 November 2015: window leaking condition at B1/F of Building A



20 November 2015: current status photos of upstand beam at B1/F of Building B



20 November 2015: current status photos of the interior of B1/F of Building B



20 November 2015: current status photos of flooded office at B1/F of Building B




20 November 2015: staircase at B1/F of Building B




20 November 2015: hallway at B1/F of Building B



20 November 2015: piping closet at B1/F of Building B



Pre-renovation 1/F floor plan



20 November 2015: staircase from 1/F to B1/F



20 November 2015: old office building condition prior to the renovation



20 November 2015: 1/F, engine room



20 November 2015: 1/F, stairway



20 November 2015: 1/F, lobby



20 November 2015: 1/F, hallway




20 November 2015: 1/F, restroom



20 November 2015: 1/F, switch box



Pre-renovation 2/F floor plan




20 November 2015: 2/F, office



20 November 2015: 2/F, hallway



20 November 2015: 2/F, stairway

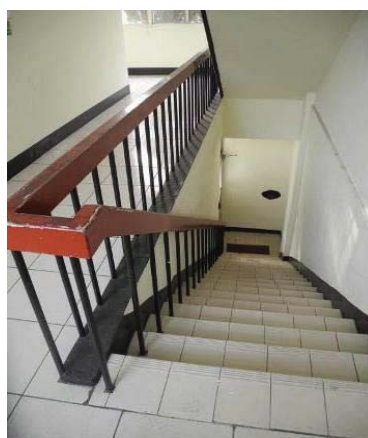


20 November 2015: 2/F, stairway



20 November 2015: 2/F, balcony

Pre-renovation 3/F floor plan



20 November 2015: 3/F, office



20 November 2015: 3/F, restroom



20 November 2015: 3/F, hallway




20 November 2015: 3/F, stairway



20 November 2015: 3/F, fire hydrant cabinet



Pre-renovation 4/F floor plan



20 November 2015: 4/F, outdoor distribution box



20 November 2015: 4/F (outside)



20 November 2015: 4/F (inside)



20 November 2015: 4/F, corridor



20 November 2015: 4/F, roof



20 November 2015: 4/F (outside)




20 November 2015: 4/F, roof



20 November 2015: 4/F, existing flower bed



20 November 2015: 4/F, water tower

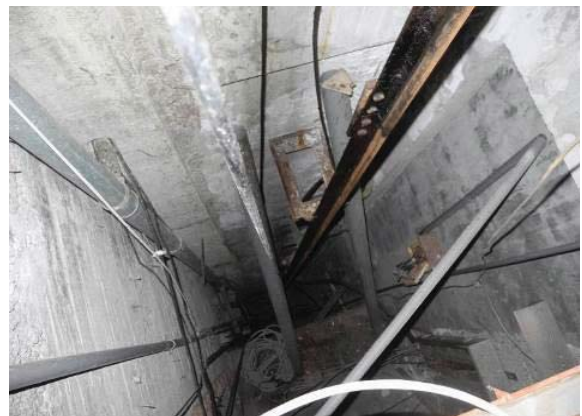

20 November 2015: 4/F, piping closet




VI. Post-Renovation Floor Plan and Photos

The use of each floor of Office 3

- B1/F: Assistant Probation Officer Room, Association for Victims Support, the Prosecutors Association, digital evidence collection training center.
- 1/F: 1 Investigation Room, 12 Inquiry Rooms, Forensic Medical Examiner Office, Taiwan After-care Association, Digital Evidence Collection Room.
- 2/F: Prosecutor Investigator Office, Accounting Office, Personnel Office, Information Management Office, Head Prosecutor Office.
- 3/F: Public Prosecutor Office, Public Prosecution Clerk Office, Intern Judge Office, Prosecutor Research Room.
- 4/F: Civil Service Ethics Office, Cashier Office, Personnel Office's storage, Accounting Office's storage, New Legal Know-how Promotion & Training Center

B1/F floor plan after the renovation

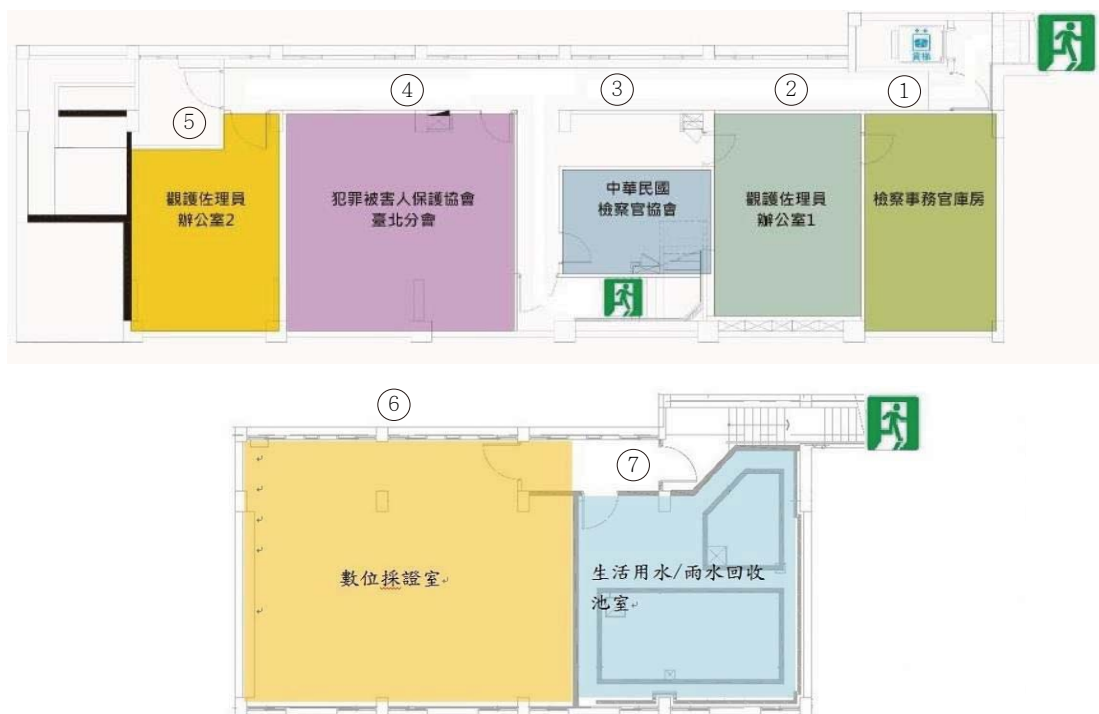

- | | | |
|--------------------------------------|---|------------------------|
| ① Prosecutor Investigator's Storage | ④ Association for Victims Support | ⑦ Water Recycling Room |
| ② Assistant Probation Officer Room 1 | ⑤ Assistant Probation Officer Room 2 | |
| ③ The Prosecutor Association | ⑥ Digital Evidence Collection Training Center | |



29 January 2018: hallway at B1/F of Building B



29 January 2018: B1/F, Association for Victims Support



18 December 2018:
B1/F, Assistant Probation Officer Room




28 August 2018: B1/F, water recycling room



29 January 2018:
staircase entrance from 1/F to B1/F



29 January 2018:
staircase entrance from B1/F to 1/F

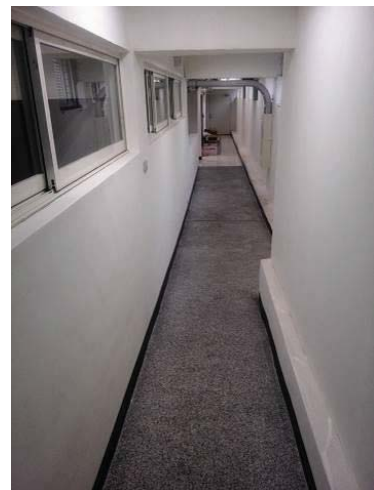

29 January 2018:
hallway at B1/F of Building B



1/F floor plan after the renovation



- | | | |
|----------------------|---------------------|------------------------------------|
| ① Inquiry Room 2 | ⑧ Inquiry Room 11 | ⑮ Counseling Room 1 |
| ② Inquiry Room 4 | ⑨ Inquiry Room 9 | ⑯ Forensic Medical Examiner Office |
| ③ Inquiry Room 6 | ⑩ Inquiry Room 7 | ⑰ Drug Information Room |
| ④ Inquiry Room 8 | ⑪ Inquiry Room 5 | ⑱ Taiwan After-Care Association |
| ⑤ Inquiry Room 10 | ⑫ Inquiry Room 3 | ⑲ Information Counter |
| ⑥ Inquiry Room 12 | ⑬ Inquiry Room 1 | ⑳ Waiting Area |
| ⑦ Investigation Room | ⑭ Counseling Room 2 | |



30 October 2018: 1/F, lobby entrance staircase



29 January 2018: 1/F, lobby waiting area



18 December 2018: 1/F, lobby



29 January 2018: 1/F, inquiry rooms hallway




18 December 2017: 1/F, Taiwan After-care Association



18 December 2017: 1/F, Forensic Medical Examiner Office




08 January 2018: Investigation Room at 1/F

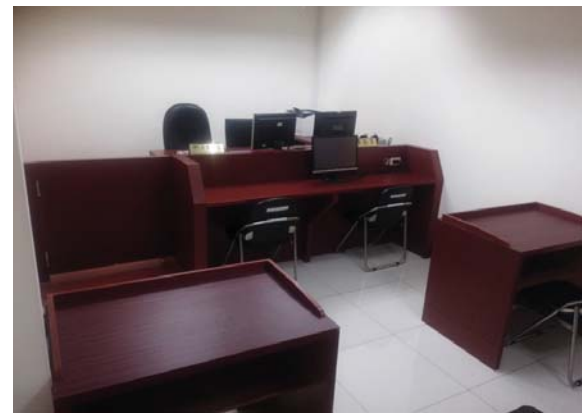

30 October 2018: 1/F, Inquiry Room



2/F floor plan after the renovation

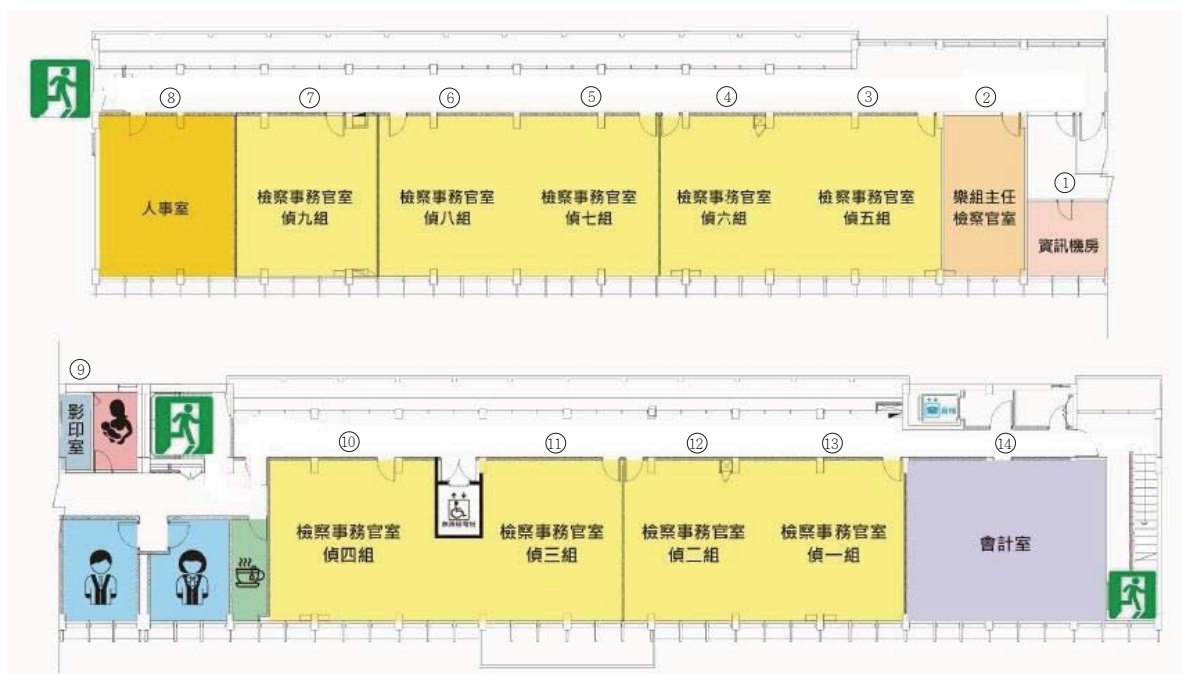

- | | | |
|--|--|--|
| ① INFORMATION Management Office | ⑥ Prosecutor Investigator Office (Investigator Team 8) | ⑪ Prosecutor Investigator Office (Investigator Team 3) |
| ② Head Prosecutor Office (Unit Le) | ⑦ Prosecutor Investigator Office (Investigator Team 9) | ⑫ Prosecutor Investigator Office (Investigator Team 2) |
| ③ Prosecutor Investigator Office (Investigator Team 5) | ⑧ Personnel Office | ⑬ Prosecutor Investigator Office (Investigator Team 1) |
| ④ Prosecutor Investigator Office (Investigator Team 6) | ⑨ Photocopy Room | |
| ⑤ Prosecutor Investigator Office (Investigator Team 7) | ⑩ Prosecutor Investigator Office (Investigator Team 4) | ⑭ Accounting Office |



29 January 2018: 2/F, Prosecutor Investigator Office



18 December 2017: 2/F, Accounting Office



29 January 2018: hallway at 2/F of Building B



29 January 2018: hallway at 2/F of Building A



29 January 2018: 2/F, restroom & nursing room



18 December 2017: 2/F, Personnel Office




18 December 2017: 2/F pantry



30 October 2018: 2/F, Information Management Office



3/F floor plan after the renovation

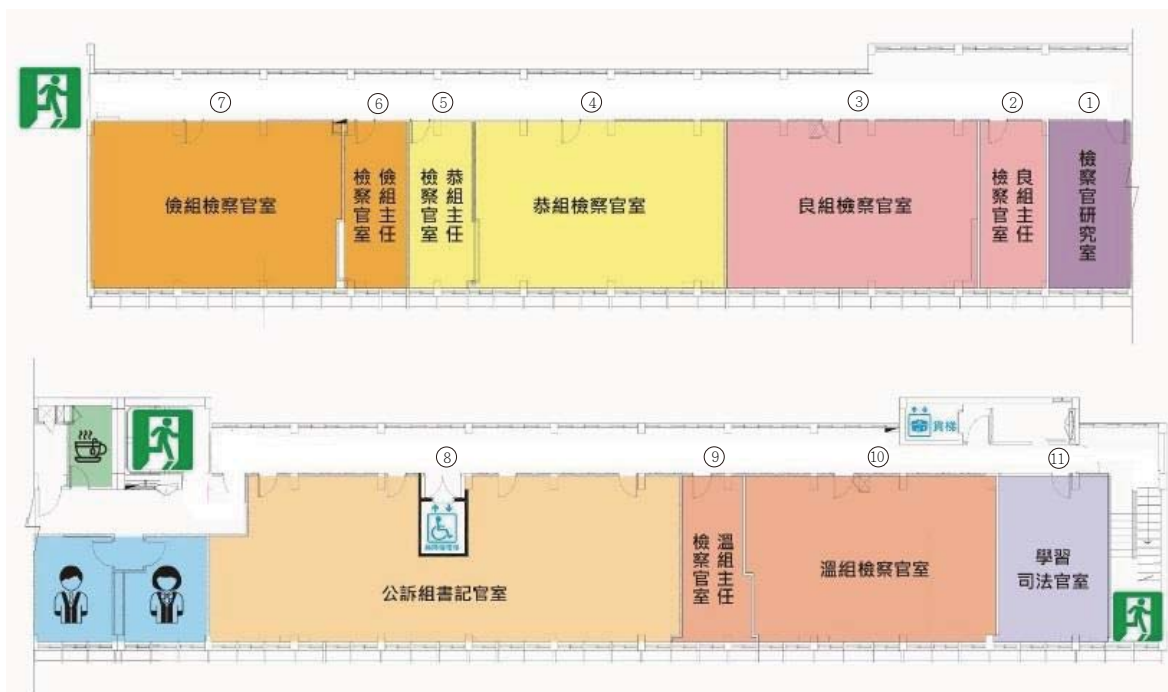

- | | | |
|---------------------------------------|--------------------------------------|-------------------------------------|
| ① Prosecutor Research Room | ⑤ Head Prosecutor Office (Unit Gong) | ⑨ Head Prosecutor Office (Unit Wen) |
| ② Head Prosecutor Office (Unit Liang) | ⑥ Head Prosecutor Office (Unit Jian) | ⑩ Prosecutor Office (Unit Wen) |
| ③ Prosecutor Office (Unit Liang) | ⑦ Prosecutor Office (Unit Jian) | ⑪ Intern Judge Office |
| ④ Prosecutor Office (Unit Gong) | ⑧ Public Prosecution Clerk Office | |



29 January 2018: 3/F, Prosecutor Research Room



29 January 2018: hallway at 3/F of Building A



17 August 2018: 3/F, Public Prosecutor Office



29 January 2018: 3/F, restroom



29 January 2018: 3/F, Public Prosecution Clerk Office



29 January 2018: 3/F, pantry




4/F floor plan after the renovation



- ① New Legal Know-How Promotion & Training Center
- ② Cashier Office
- ③ Personnel Office's Storage

- ④ Accounting Office's storage
- ⑤ Civil Service Ethics Office

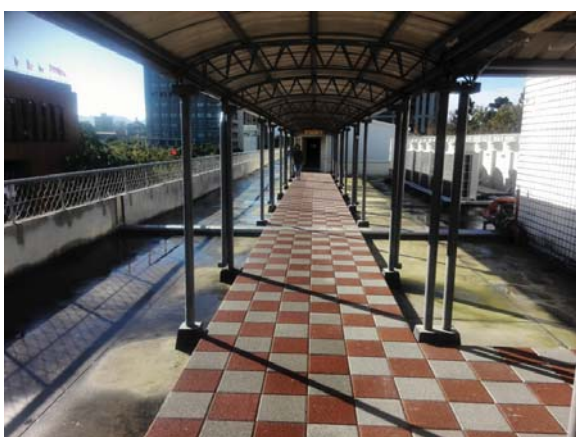

29 January 2018: 4/F, corridor



29 January 2018: 4/F, VRV air-conditioner compressor (outdoor)



29 January 2018: 4/F, Cashier Office



29 January 2018: 4/F, corridor



29 January 2018: 4/F, corridor



29 January 2018: 4/F, offices



30 October 2018: 4/F, New Legal Know-how Promotion & Training Center



30 October 2018: 4/F, New Legal Know-how Promotion & Training Center




VII. Important Milestones

23 / May. 2016	The Executive Yuan approved the revised total costs of NT\$92,702,000 for the plan.
02 / Aug. 2016	Completed basic design review.
31 / Aug. 2016	Completed the detailed design.
06 / Sep. 2016	Opened for public viewing; after 3 unsuccessful bidding on 14 September, 4 October and 20 October 2016, the bidding was successful rewarded on 18 November 2016.
27 / Nov. 2016	Commencement of the Procurement Building.
16 / June. 2017	First design change.
29 / Sep. 2017	Public Prosecution Section of the Office moved to 3/F of the Procurement Building.
11 / Oct. 2017	Second design change.
16 / Nov. 2017	Civil Service Ethics Office of the Office moved to 4/F of the Procurement Building.
25 / Nov. 2017	Completion of the Procurement Building.
01 / Dec. 2017	Prosecutor Investigators of Office 3 moved to 2/F of the Procurement Building.
08 / Dec. 2017	Association for Victims Support, Taiwan After-care Association, the Prosecutors Association, Forensic Medical Examiner Office, Personnel Office, Accounting Office and Cashier Office of Office 4 moved to 1/F, 2/F and 4/F of the Procurement Building basement.
08 / Feb. 2018	Opening ceremony of Office 3.
23 / Apr. 2018	Completion of the New Legal Know-how Promotion & Training Center.

VIII. Process of Design Changes

A. The Construction Period and Amount Increased due to First Design Change on 16 June 2017


The original contract was NT\$69,880,000, which became NT\$75,957,347 after the change, and the completion date set at 5 October 2017 (construction period increased from 270 days to 313 days). The first design change took place because the original concrete was low in strength with poor floor slab thickness and reinforcement, the basement leak was severe, the roof required heat insulation, the rebar truss and corridor on 4/F was severely rusted, VRV and related electromechanical equipment were insufficient and in need of an expansion, the entrance stairs requires improvements, and, upon the Chief Prosecutor made a visit on 9 May 2017, it was instructed that 1/F circulation must be adjust to leave no security or visual blind spot.

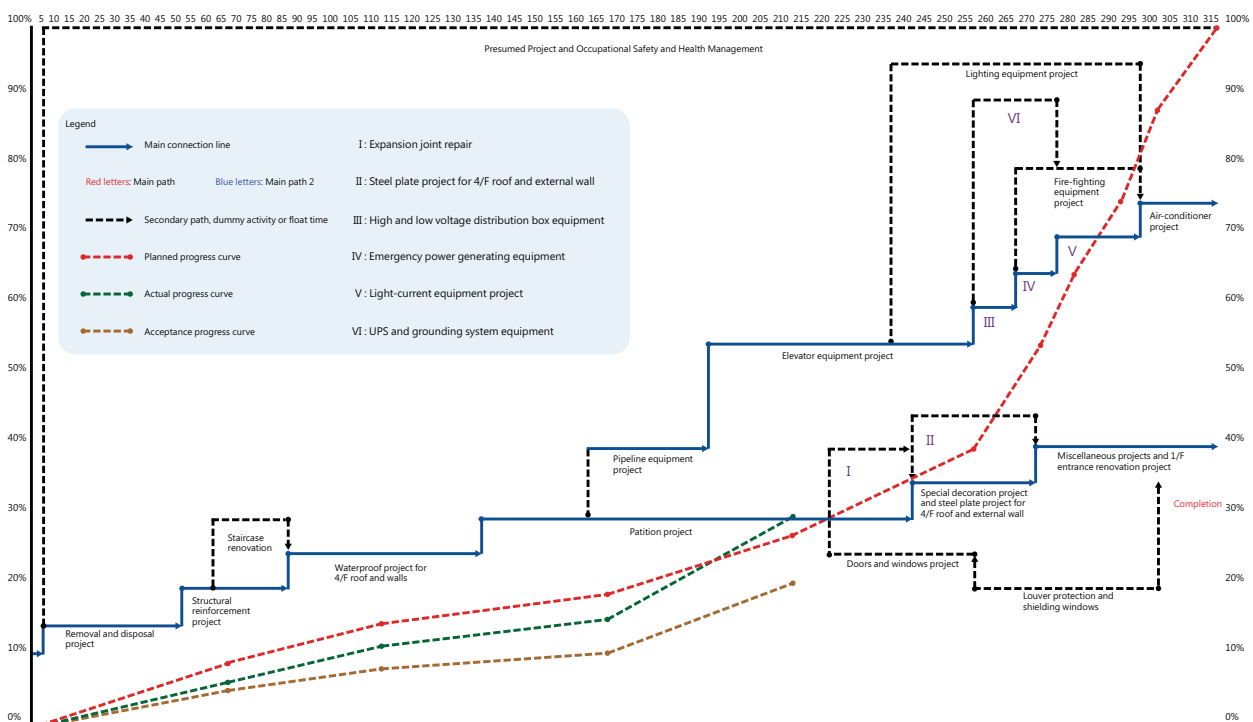

Renovation Project for the Offices in the Procurement Building of Taiwan Taipei District Court Prosecutors Office
(in line with the first revision)




Original contracted design (prior to the change)

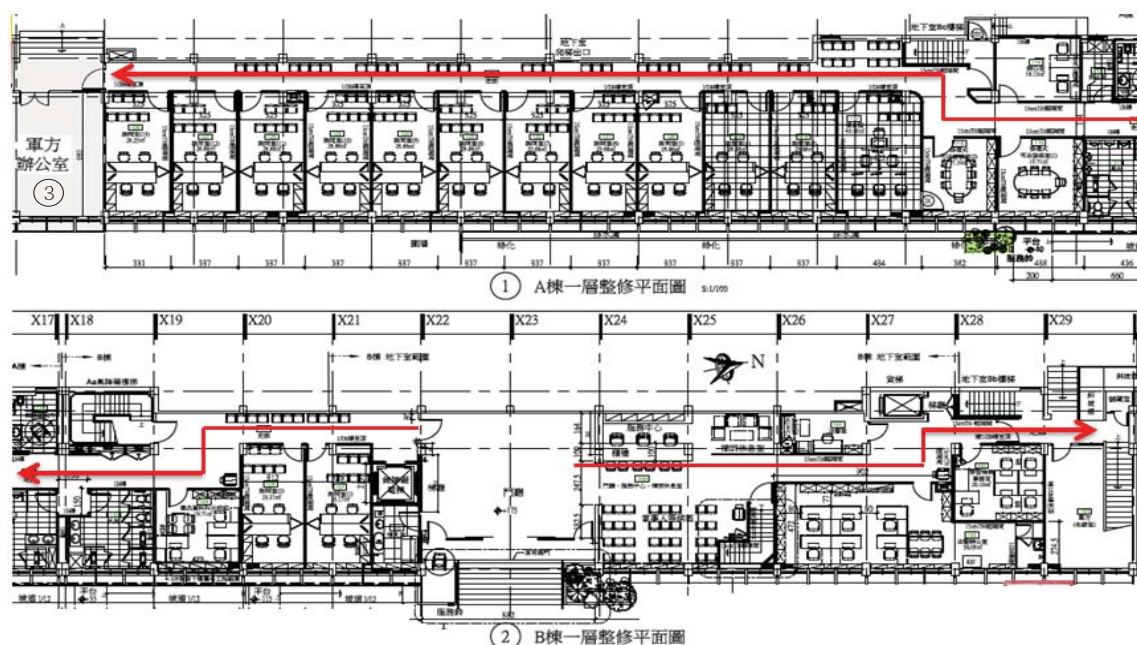

① Renovation Floor Plan for 1/F of Building A ② Renovation Floor Plan for 1/F of Building B ③ Military Offices

After the Chief Prosecutor made a visit on 9 May 2017, it was instructed that the circulation shall be secure without any visual blind spot (after the change)

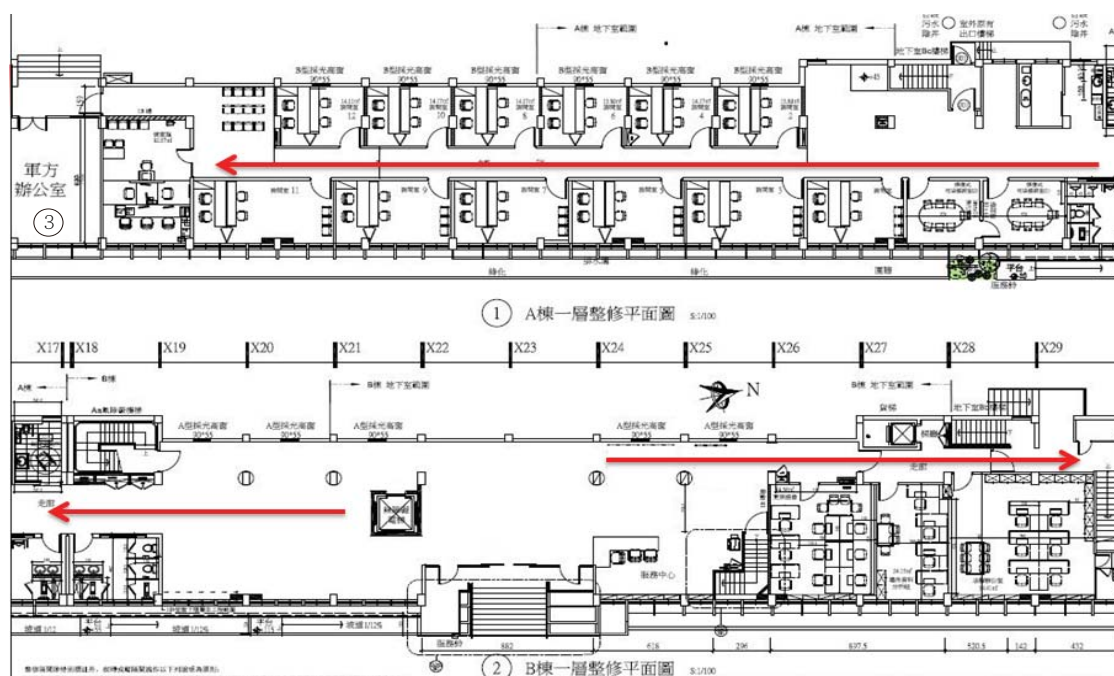

① Renovation Floor Plan for 1/F of Building A ② Renovation Floor Plan for 1/F of Building B ③ Military Offices




20 April 2017: poor structure





20 April 2017: construct waterproof slope



2 March 2017: rusted roof struss

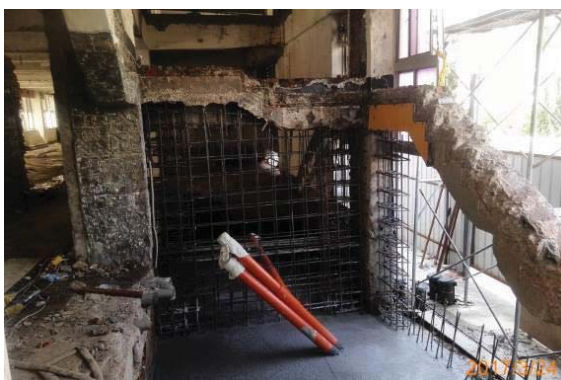

24 March 2017: demolish old staircase and rebuild new staircase

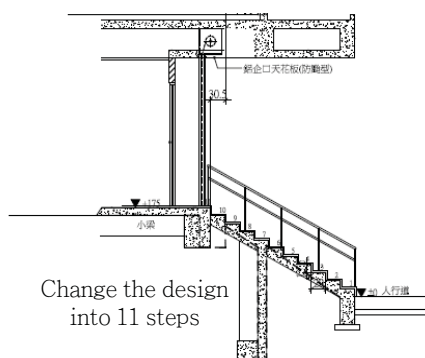

Reduce slope of the entrance stairs



18 April 2017: adjust depth of the dumbwaiter manhole



8 May 2017: dumbwaiter manhole water seepage




12 June 2017: basement water seepage treatment




B. The construction period and amount increased due to second design change on 11 October 2017

The contract amount was NT\$78,544,238 after the change, and the completion date set at 26 November 2017 (construction period increased from 313 days to 365 days). The second design change took place because the 1/F office space required adjustment, the 2/F and 3/F required hallway ceilings and curtain box, power cables required an upgrade, the Counseling Room required adjustment on wooden renovation, and the air-conditioning project required adjustment.

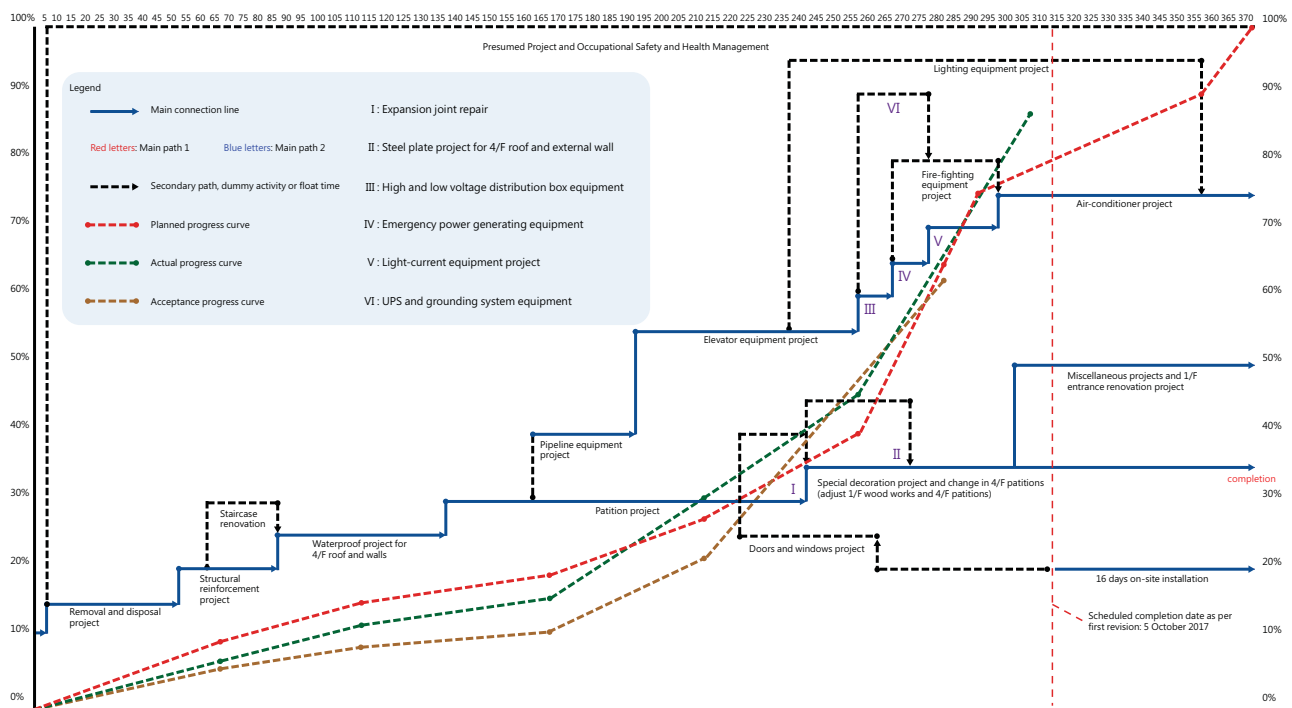


Project for the Offices in the Procurement Building of Taiwan Taipei District Court Prosecutors Office
(in line with the second revision)



IX. Project Difficulties and Solutions

- There was no original design drawing for the Project, which caused the differences between the initial design drawing and the actual construction.
- Solution: After requesting the technicians to perform on-site survey, the construction was adjusted in line with the existing status.

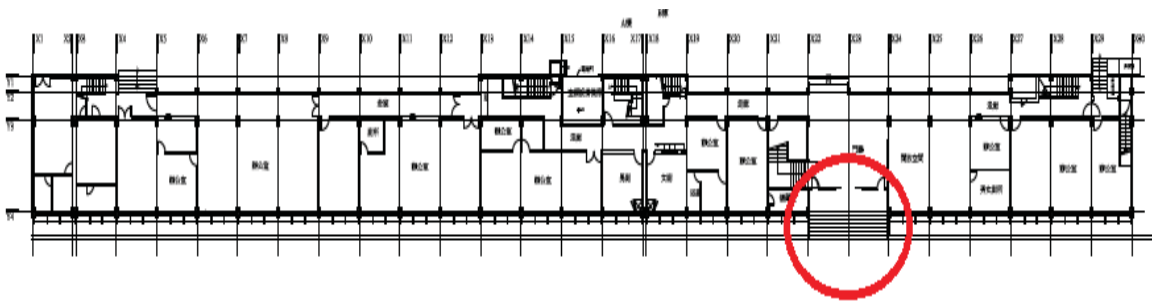

1/F existing status floor plan

- The Project is a long and narrow type. There was only one entrance/exit for cleaning operations at the site, and the amount of debris was more than expected. The structure is fragile, cannot use machine to carry out indoor demolition, and there were unidentified military pipelines which affected the construction.
- Solution: On 23 February 2017, it was negotiated and agreed that the machine can access the camp on weekdays; on 28 February 2017, the military moves out from space of X1~X4; on 10 March 2017, consent was obtained to remove the coconut tree outside of F3 base location, and negotiated with the military to construct ramp at the F2 base location to facilitate the transportation of machines and materials; on 3 June 2017, it was negotiated and agreed to reallocate all pipelines.



31 December 2016:w single entrance/exit



17 January 2017: huge amount of debris



14 February 2017: technician perform on-site survey



23 March 2017: ramp access at F2 base



10 March 2017: remove the coconut tree outside F3 base



23 March 2017: military allowed construction time and area



- Concrete was low in strength with poor reinforcement, the basement leak was severe
- Solution: Structural floor reinforcement applied on 2/F and 3/F
- Solution: Adopt water-conductive gravel layer, drain, catch, sewer manhole for drainage.



20 April 2017: floor slab used only single layer of No.2 reinforcement



22 May 2017: floor slab reinforcement




12 June 2017: the basement leak was severe



18 September 2017: drain water by crushed stone & non-woven fabric

X. Project Supervision Team and Supervision Records

The organizer held a pre-construction meeting with the contractors before the commencement, instructing that, in order to complete on 25 December 2017 and smoothly hold Office 3 opening ceremony on 8 February 2018, there shall be personnel dispatched on daily basis to conduct on-site supervision (and take turns during holidays), the project supervision meeting shall be held on weekly (a total of 54 weekly supervision meetings) and monthly (a total of 12 monthly supervision meetings) basis until the completion, Prosecutor Investigator LIEN YANG who has civil engineering, structure, geotechnical qualification shall be assigned to assist the architect and Taiyi Construction in solving site affairs, and LINE group shall be utilized during the period to solve site issues promptly.



The Project obtained approval from Chief Prosecutor on July 2015 to set up the project supervory team





16 May 2017: monthly supervisory meeting



25 February 2017: Head Prosecutor came to supervise



18 April 2017: Chief Prosecutor carried out on-site supervision



18 April 2017: Chief Prosecutor carried out on-site supervision



XI. Set-Up Process of Office 3 and Digital Evidence Collection Room

Taiwan Taipei District Prosecutors Office was established on 1 November 1945. Due to economic prosperity in its juridical area, there are many issues causing inconvenience in operation such as the increasing number of litigation cases accepted every year, the expanded staff quota, and the scattered office buildings. For a long-term fix, the Ministry of Justice had coordinated with the Ministry of National Defense to appropriate its current location, the Procurement Building of the Republic of China Armed Forces Reserve of Ministry of National Defense, to the Office, which was approved by the Ministry of National Defense.

The said building has been in use since its completion in 1964. It has been half a century; the walls were chipping off and leaking, and the equipment were outdated; it was not in compliance with the requirements of the current Building Control Act and Fire Services Act and affected the structural safety of

the building. The leaders of all levels of the Ministry of Justice coordinated to raise funds for planning and updating, then, the Executive Yuan approved a renovation fund of NT\$81,931,652, where Prosecutor Investigator, Lien Yang, shall be the organizer, Chieh Chien-Hua architect firm shall be in charge of design and supervision, and Taiyi Construction Co., Ltd. shall be in charge of construction. Structural seismic reinforcement and renovation were carried out and scheduled to be completed in 2017. It was named "Taiwan Taipei District Court Prosecutors Office - Office 3".


In order to effectively combat crimes, the Office had independently developed a drug database funded by the technology project of the Ministry of Science and Technology in 2015. During the period, it was noticed that mobile communication applications (such as Line, WeChat, etc.) are gradually replacing the traditional telephone communication and becoming

the mainstream of communication. Thus, the fund was used to purchase one unit of digital evidence collector and assigned staff members to participate in the training, learning the techniques of capturing and restoring social media image records and other information on mobile devices and unlocking mobile phone passwords, etc., which was pioneer among procuratorates in the country.

Based on the above-mentioned foundation and in order for expand the use of the above-mentioned technology, the Office has intergreted expertise of the Office's Prosecutor Investigators by having the Prosecutors lead the establishment of Digital Evidence Collection Team to train digital evidence collection talents. A total of 13 Prosecutor Investigators who are eager to learn such skill were recruited and collected evidence from more than 150 mobile devices seized in various cases as directed by the Prosecutor; now, they can independently complete digital evidence collection tasks and trace for criminal clues quickly at any time.

On 11 May 2017, the Executive Yuan adopted the New Generation Anti-drug Strategy to face drug crimes and other related issues with more effective resource integration. As for the aforementioned current situation of drug crimes committed through means of communication applications, High Court Prosecutors Office had drawn up the "Digital Evidence Collection Operations Team Establishment Plan of Taiwan High Court Prosecutors Office and Its Subordinate Prosecutors Offices" in 2018 to purchase and distribute relevant hardware equipment for evidence collection, while instructing relevant District Prosecutors Offices to set up Digital Evidence Collection Room.

The Office integrated the digital evidence collection experiences, trained skillful Investigators and supervision of the Prosecutors in the establishment of the Digital Evidence Collection Center and the followings at the Office: (1) Discussion Room; (2) Evidence Collection Room (including evidence retention); (3) drug database. On 1 February 2018, the



evidence collection operation commenced its new stage upon the opening ceremony held by the minister. It is expected that the Evidence Collection Room can provide cases with evidence collection results even more quickly under the software, hardware and human resources, enrich the evidence collection database and combat various crimes more effectively.

XII. Opening Ceremony of Office 3 and Digital Evidence Collection Room

In consideration of the current procuratorate name is easily misunderstood as being subordinate to the court as well as being inconsistent with the principle of independent prosecution from trial, National Conference on Judicial Reform removed “Court” in front of each Prosecutors Office upon resolution, thus, on the morning of 8 February 2018, all procuratorates national-wide had their name plates changed simultaneously. The Office scheduled to hold the opening ceremony of name-plate update at 11:00 am, which will be personally hosted by Minister of Justice, Chiu Tai-San and witnessed by Secretary-General of Judicial Yuan, Lu Tai-Lang, Political Deputy Minister of Justice, Chen Ming-Tang, Political Deputy Minister of Justice, Tsai Pi-Chung, Administrative Deputy Minister of Justice, Chang Tou-Hui, Section Chief of Prosecution Section of the Ministry of Justice, Lin Pang-Liang, Section Chief of Comprehensive Planning Section of the Ministry of Justice, Lin Li-Ying, Prosecutor General of Supreme Prosecutors Office, Yen Ta-He, Chief Prosecutor of Taiwan High Court Prosecutors Office, Wang Tien-Sheng, President of Judges and Prosecutors Training Institute, Tsai Pi-Yu and Chief Judge of Taiwan Taipei District Court Huang Kuo-Chung. The ceremony was simple and grand.

The opening ceremony of Office 3 and Digital Evidence Collection Room was then held at 11:20 am with Ms. Iris Liu sang a “Blessing Song” in Chinese and English under the violin accompaniment of the Office’s Substituted Civilian Serviceman, Lin Hsin-Tzu, to celebrate the completion of the office building. Ms. Iris Liu who sang the “Blessing Song” to bless “fresh new start of everlasting prosperity” is a talented young female singer and beloved daughter of the Office’s Head Prosecutor, Liu Cheng-Wu; her grandfather used to be the Chief Secretary of the Office as well. A three-generation of relationship with Taiwan Taipei District Prosecutors Office, something Taiwan Taipei District Prosecutors Office is very proud of; and it added nice judicial story with her beautiful voices left in this historical event.


At the beginning of the ceremony, Minister Chiu, Prosecutor General Yen, Chief Prosecutor Wang successively delivered speeches and congratulations to encourage the inheritance of excellent traditional and continuation of hard work to meet people’s expectations in procuratorate. Minister Chiu also presented tokens of appreciation to the director committee member of Taiwan Taiwan After-care Association Taipei Branch, Lin Ping-Yao (“Good Practice of Philanthropy”) and creator of “Libra”, Wu Tsung-Lin (“Art of Balance”). Director committee member, Lin Ping-Yao, and his team not only invested in after-care protection works, but also made many contributions in promoting social peace. In order to celebrate the completion of Office 3, the honorable attendants donated “Libra” to Taipei District Prosecutors Office. Mr. Wu Tsung-Lin, the national master of copper art is also kind enough to teach the art of bronze gongs in



8 February 2018: Chief Prosecutor gave a welcome speech



8 February 2018: the opening ceremony



8 February 2018: A group photo

the prison, hoping that the rehabilitated people will use copper as a mirror to find new value in its own life and start a new life. Furthermore, "Compassion: the entire piece was made by hand wholeheartedly, representing a group of people who abide love to achieve the goal -- neither severity nor leniency. Reason: the round shape of copper gong represents the harmony in

truth and the strictness in law. Law: libra represents the concept of equality before the law. Taiwan After-care Association Taipei Branch made and gave the Office a libra as a symbol of faith. The libra was engraved with "justice, efficiency" in Latin, which can from words of sages and men of virtue "all men are equal before the law" and "delayed justice is not justice".



8 February 2018: the minister gave a welcome speech



8 February 2018: opening ceremony of the digital evidence collection center
